







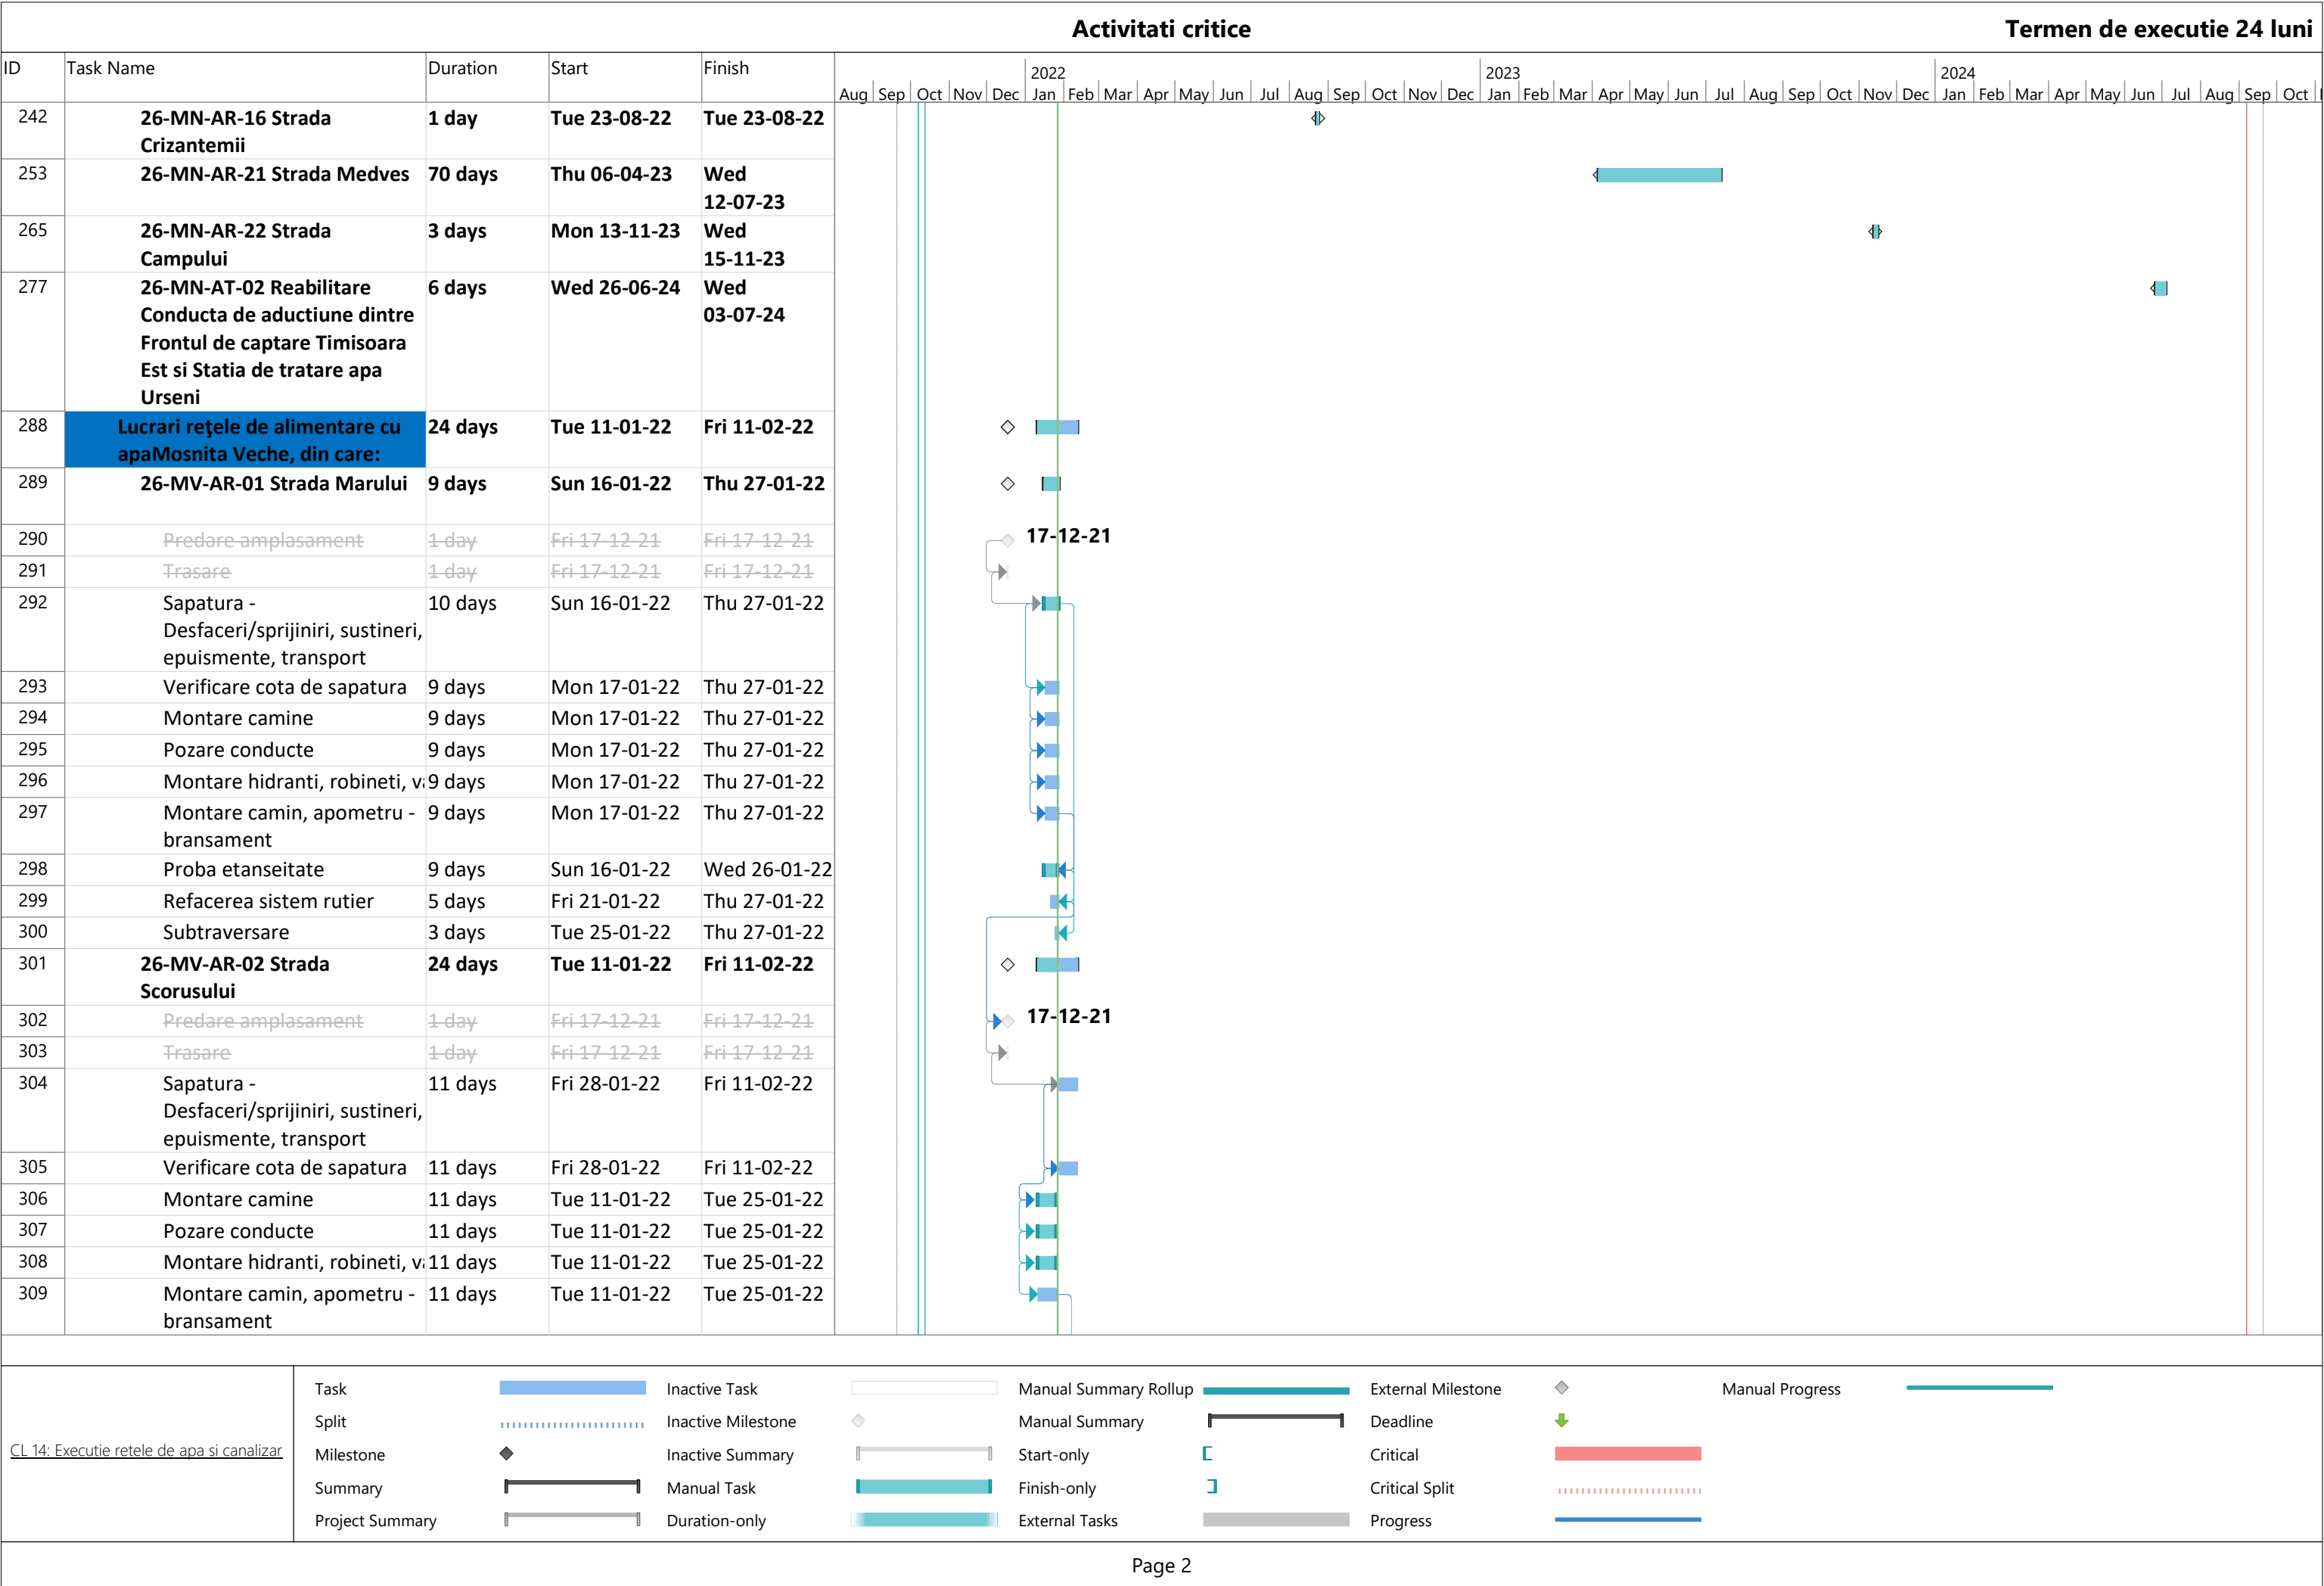

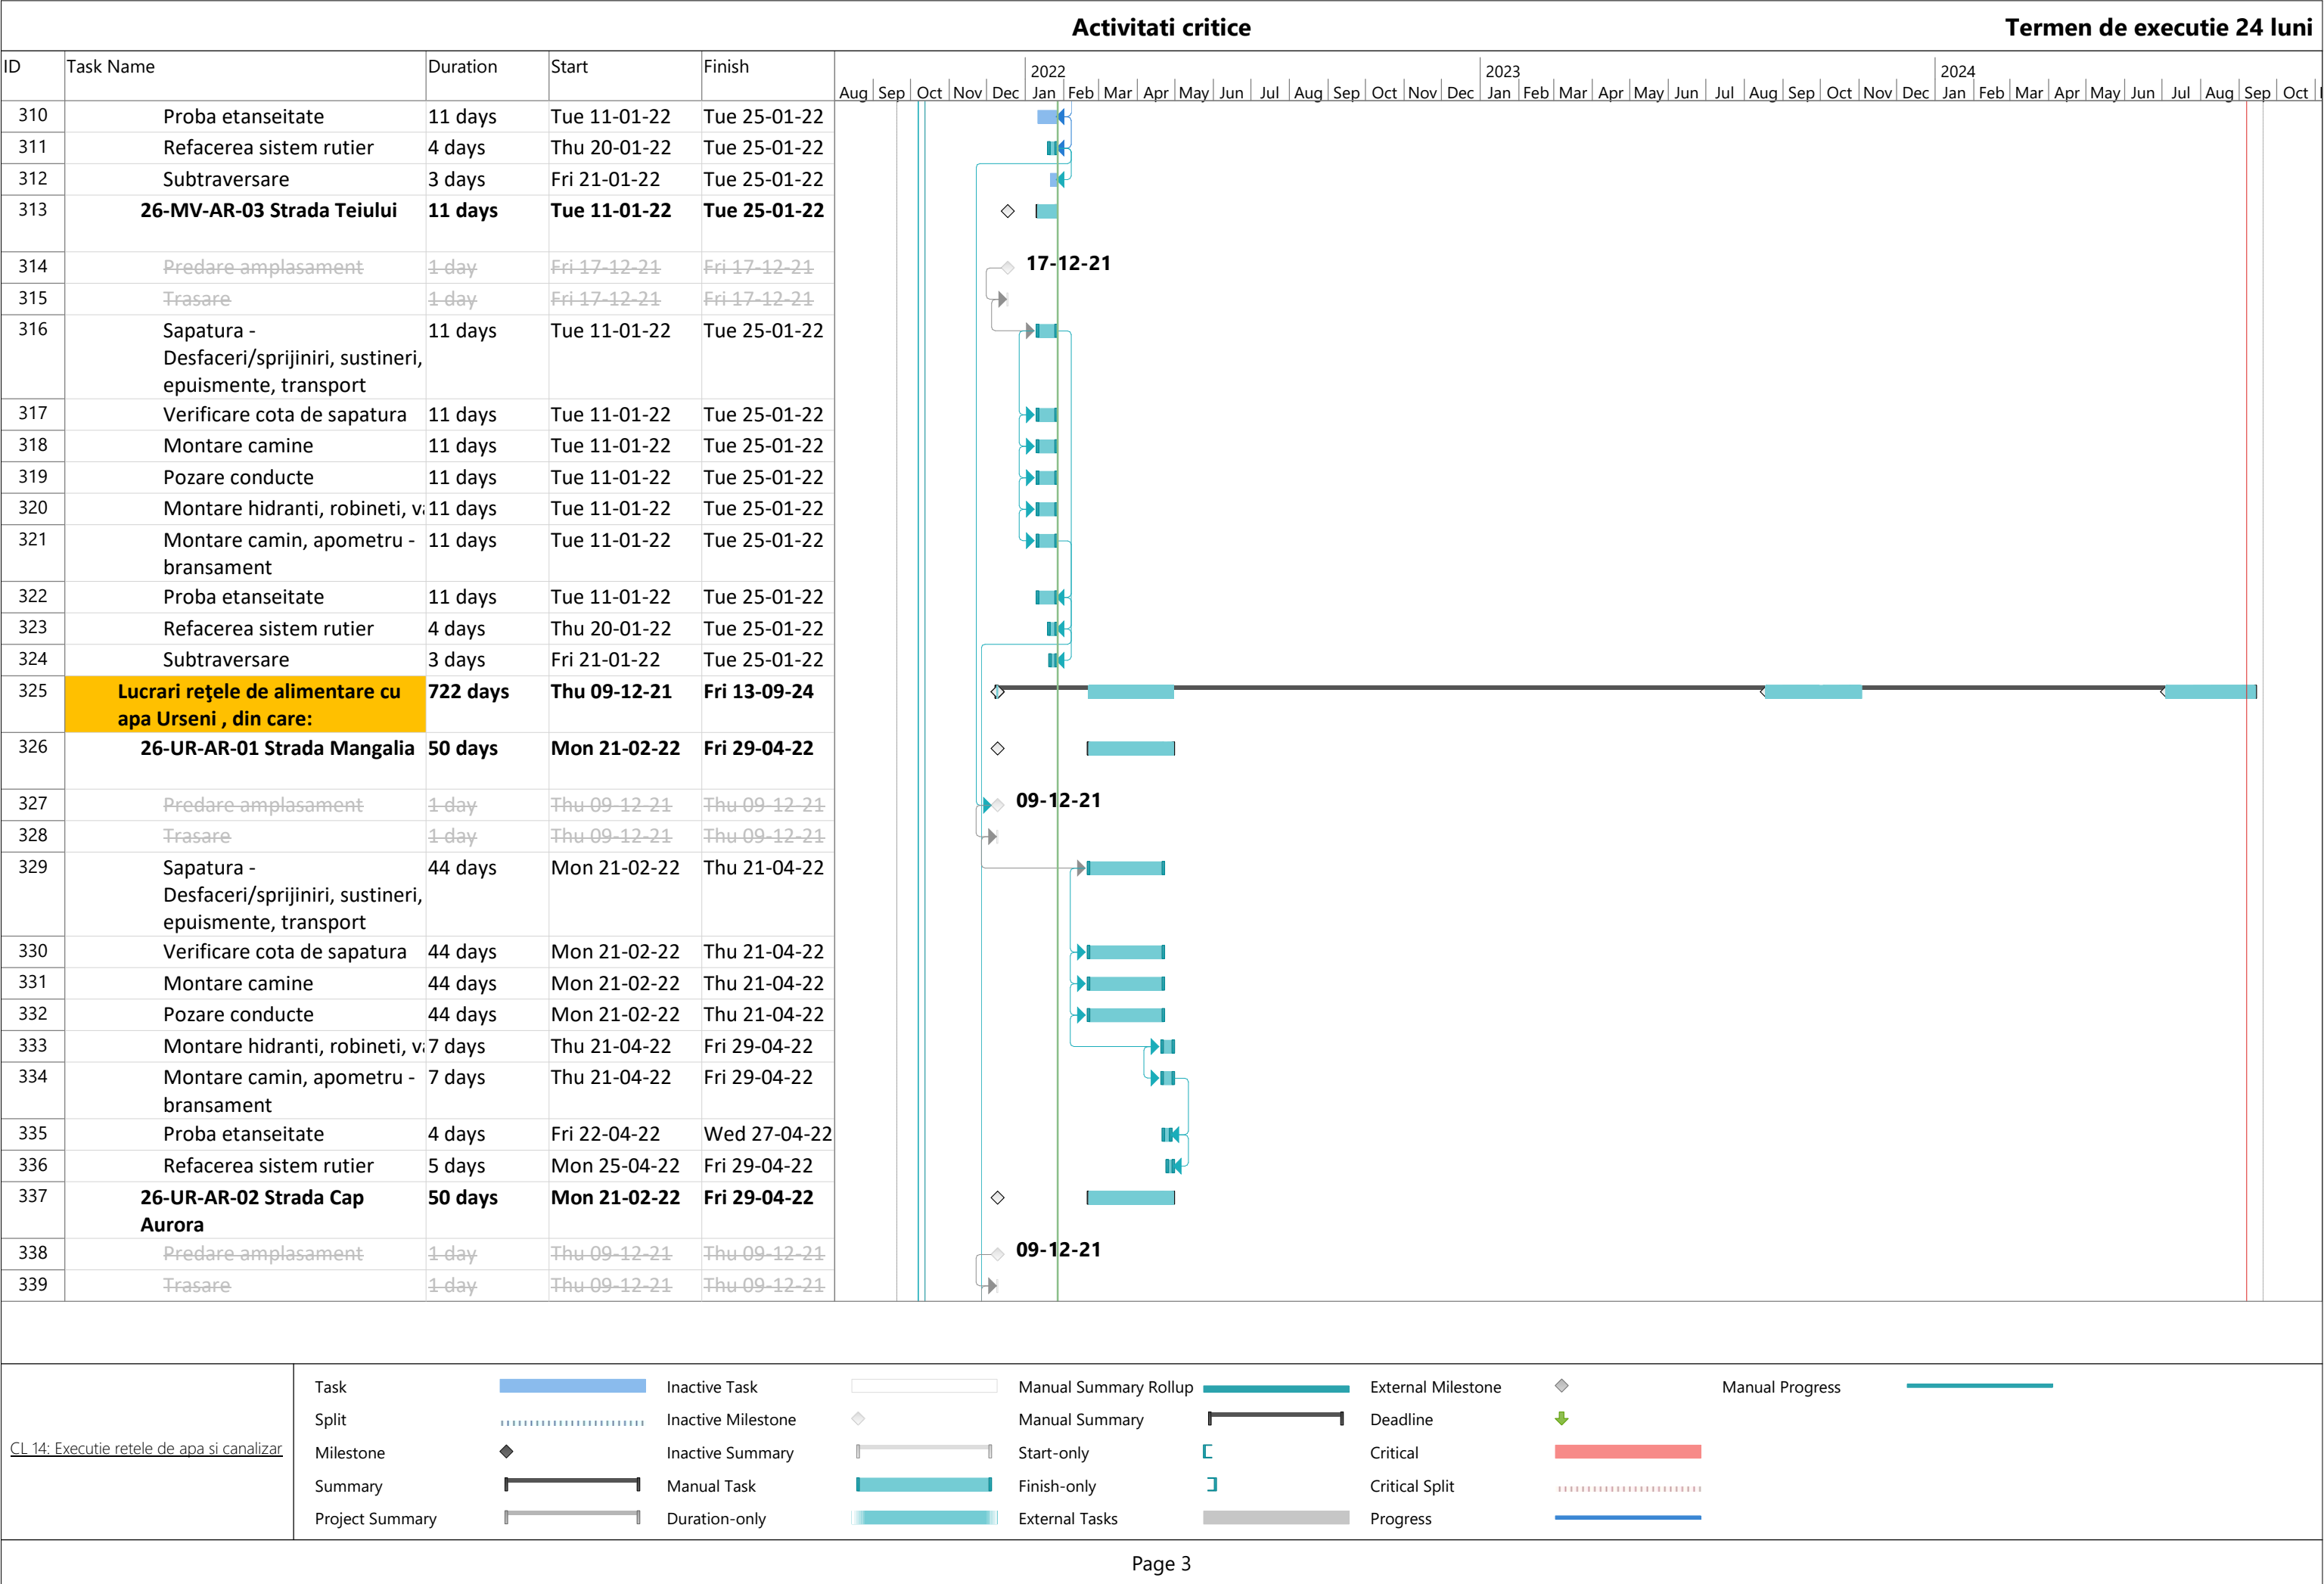

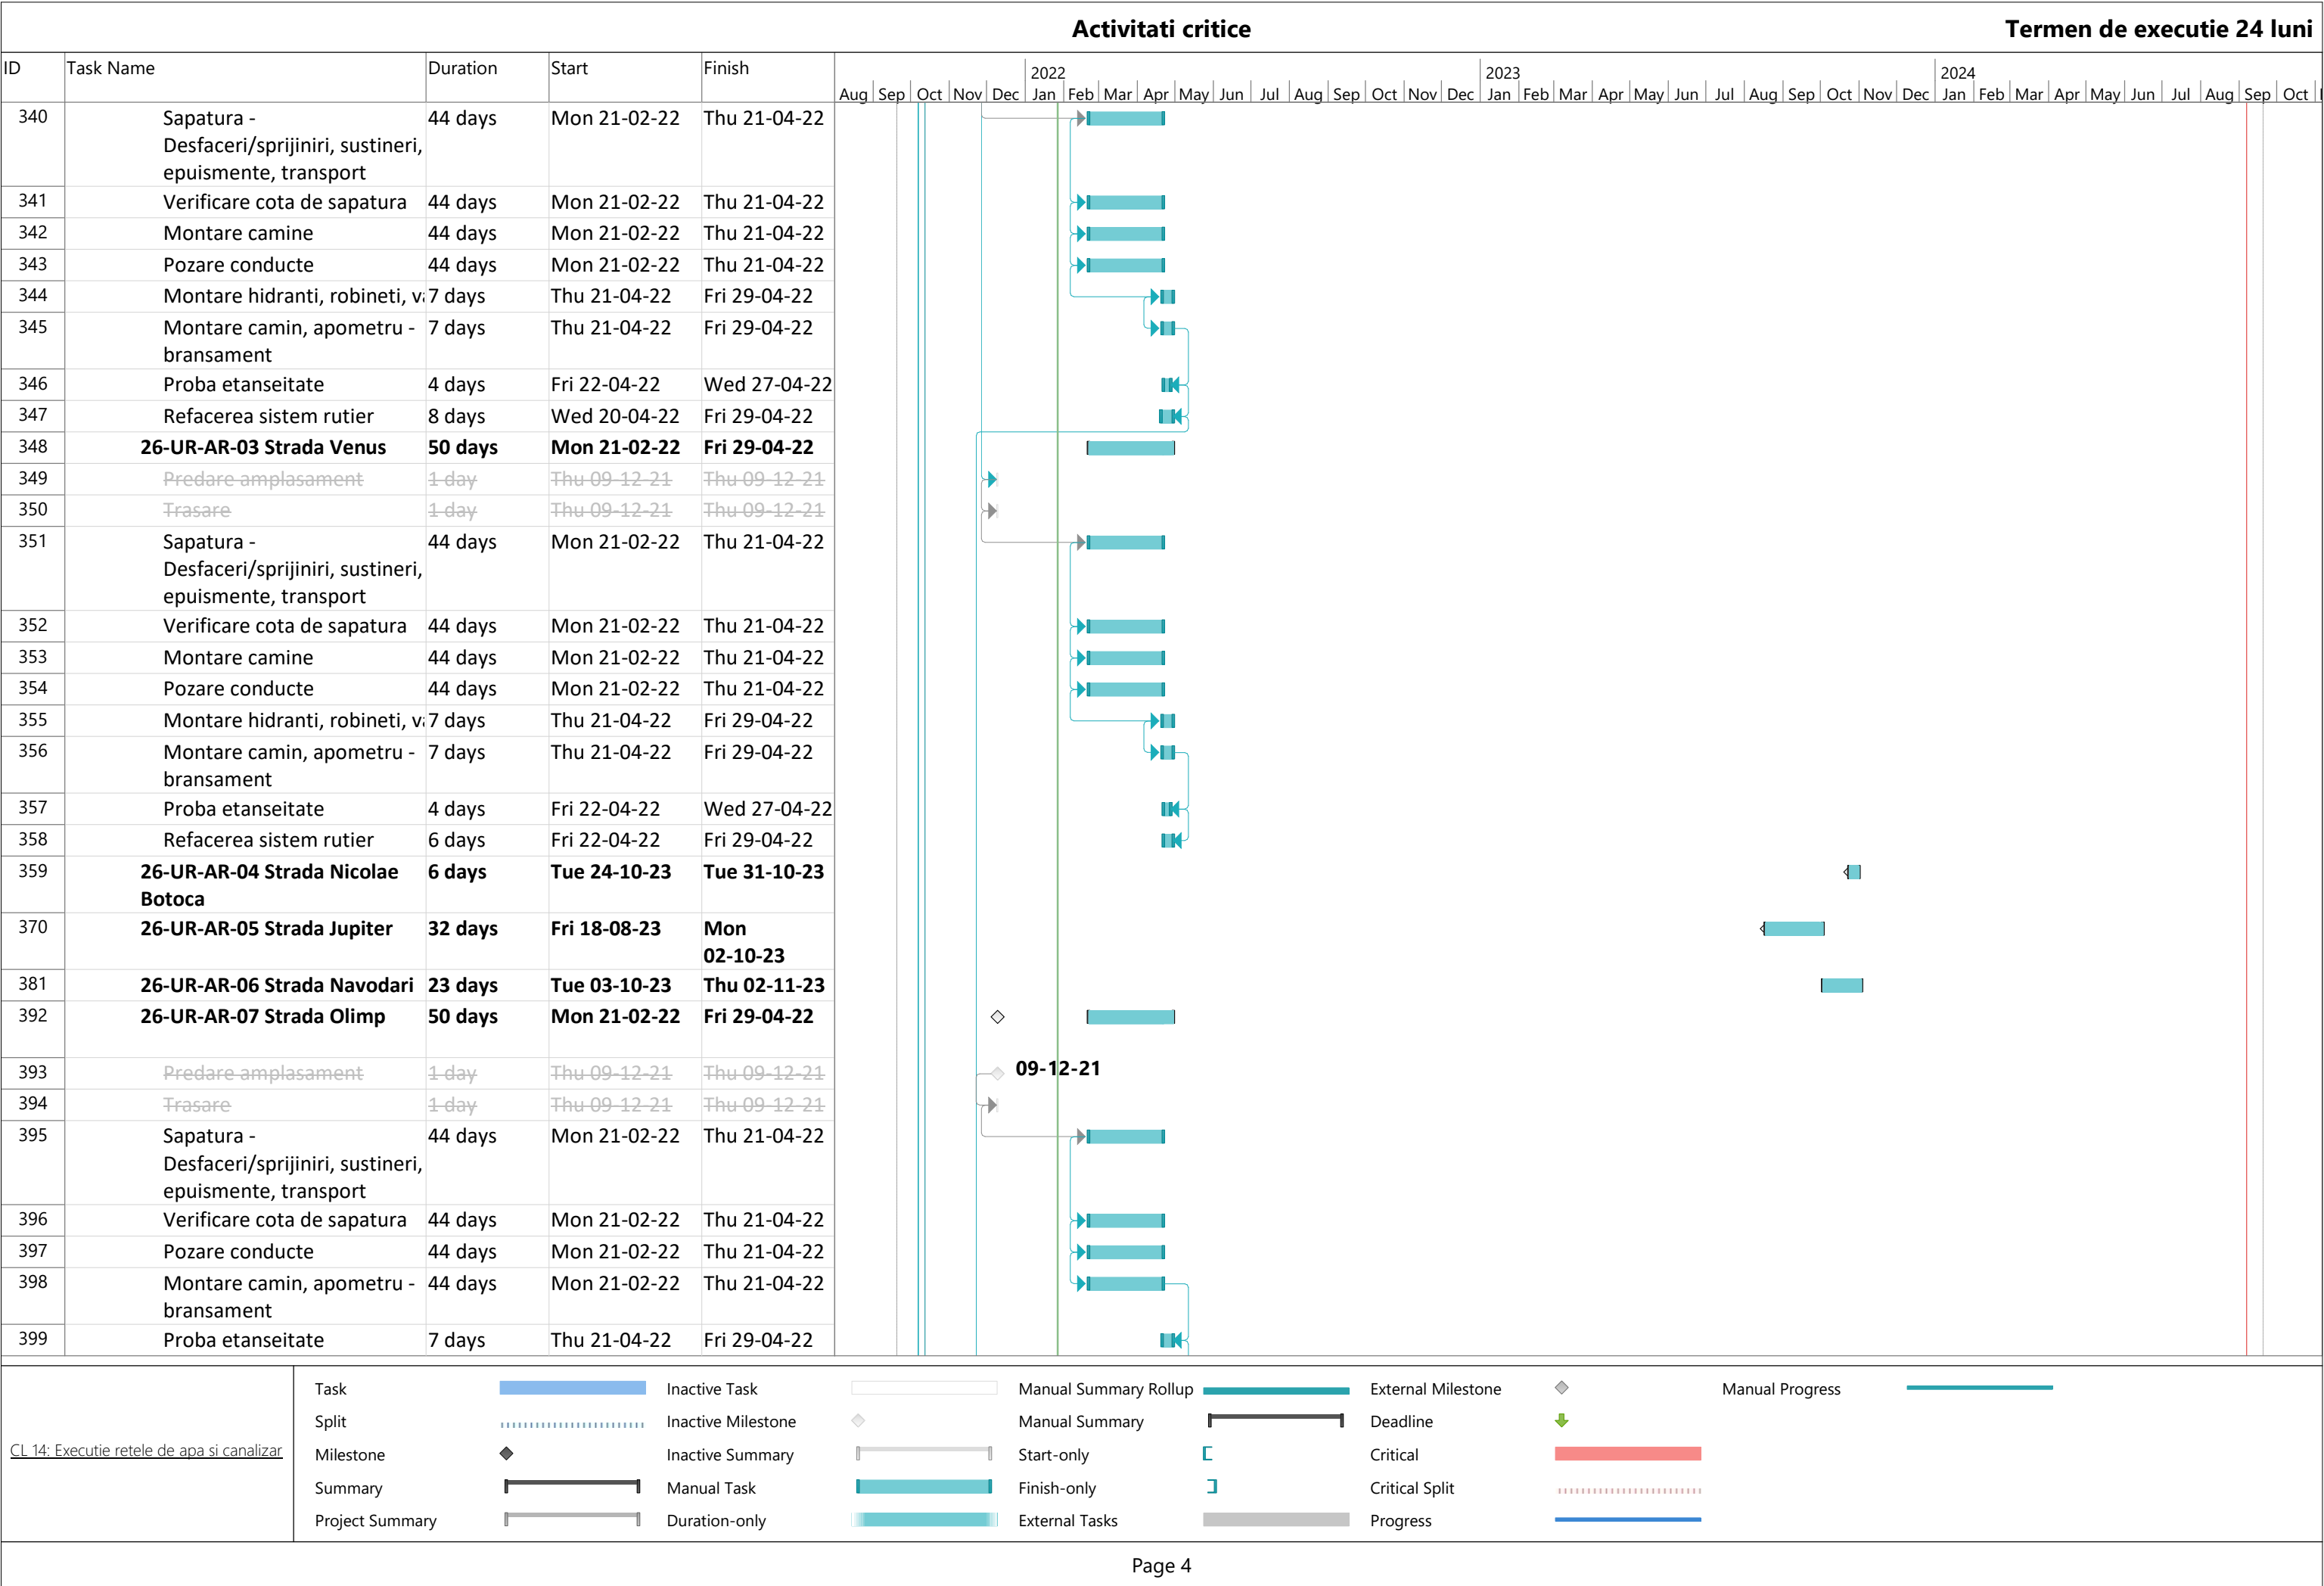


[illegible]

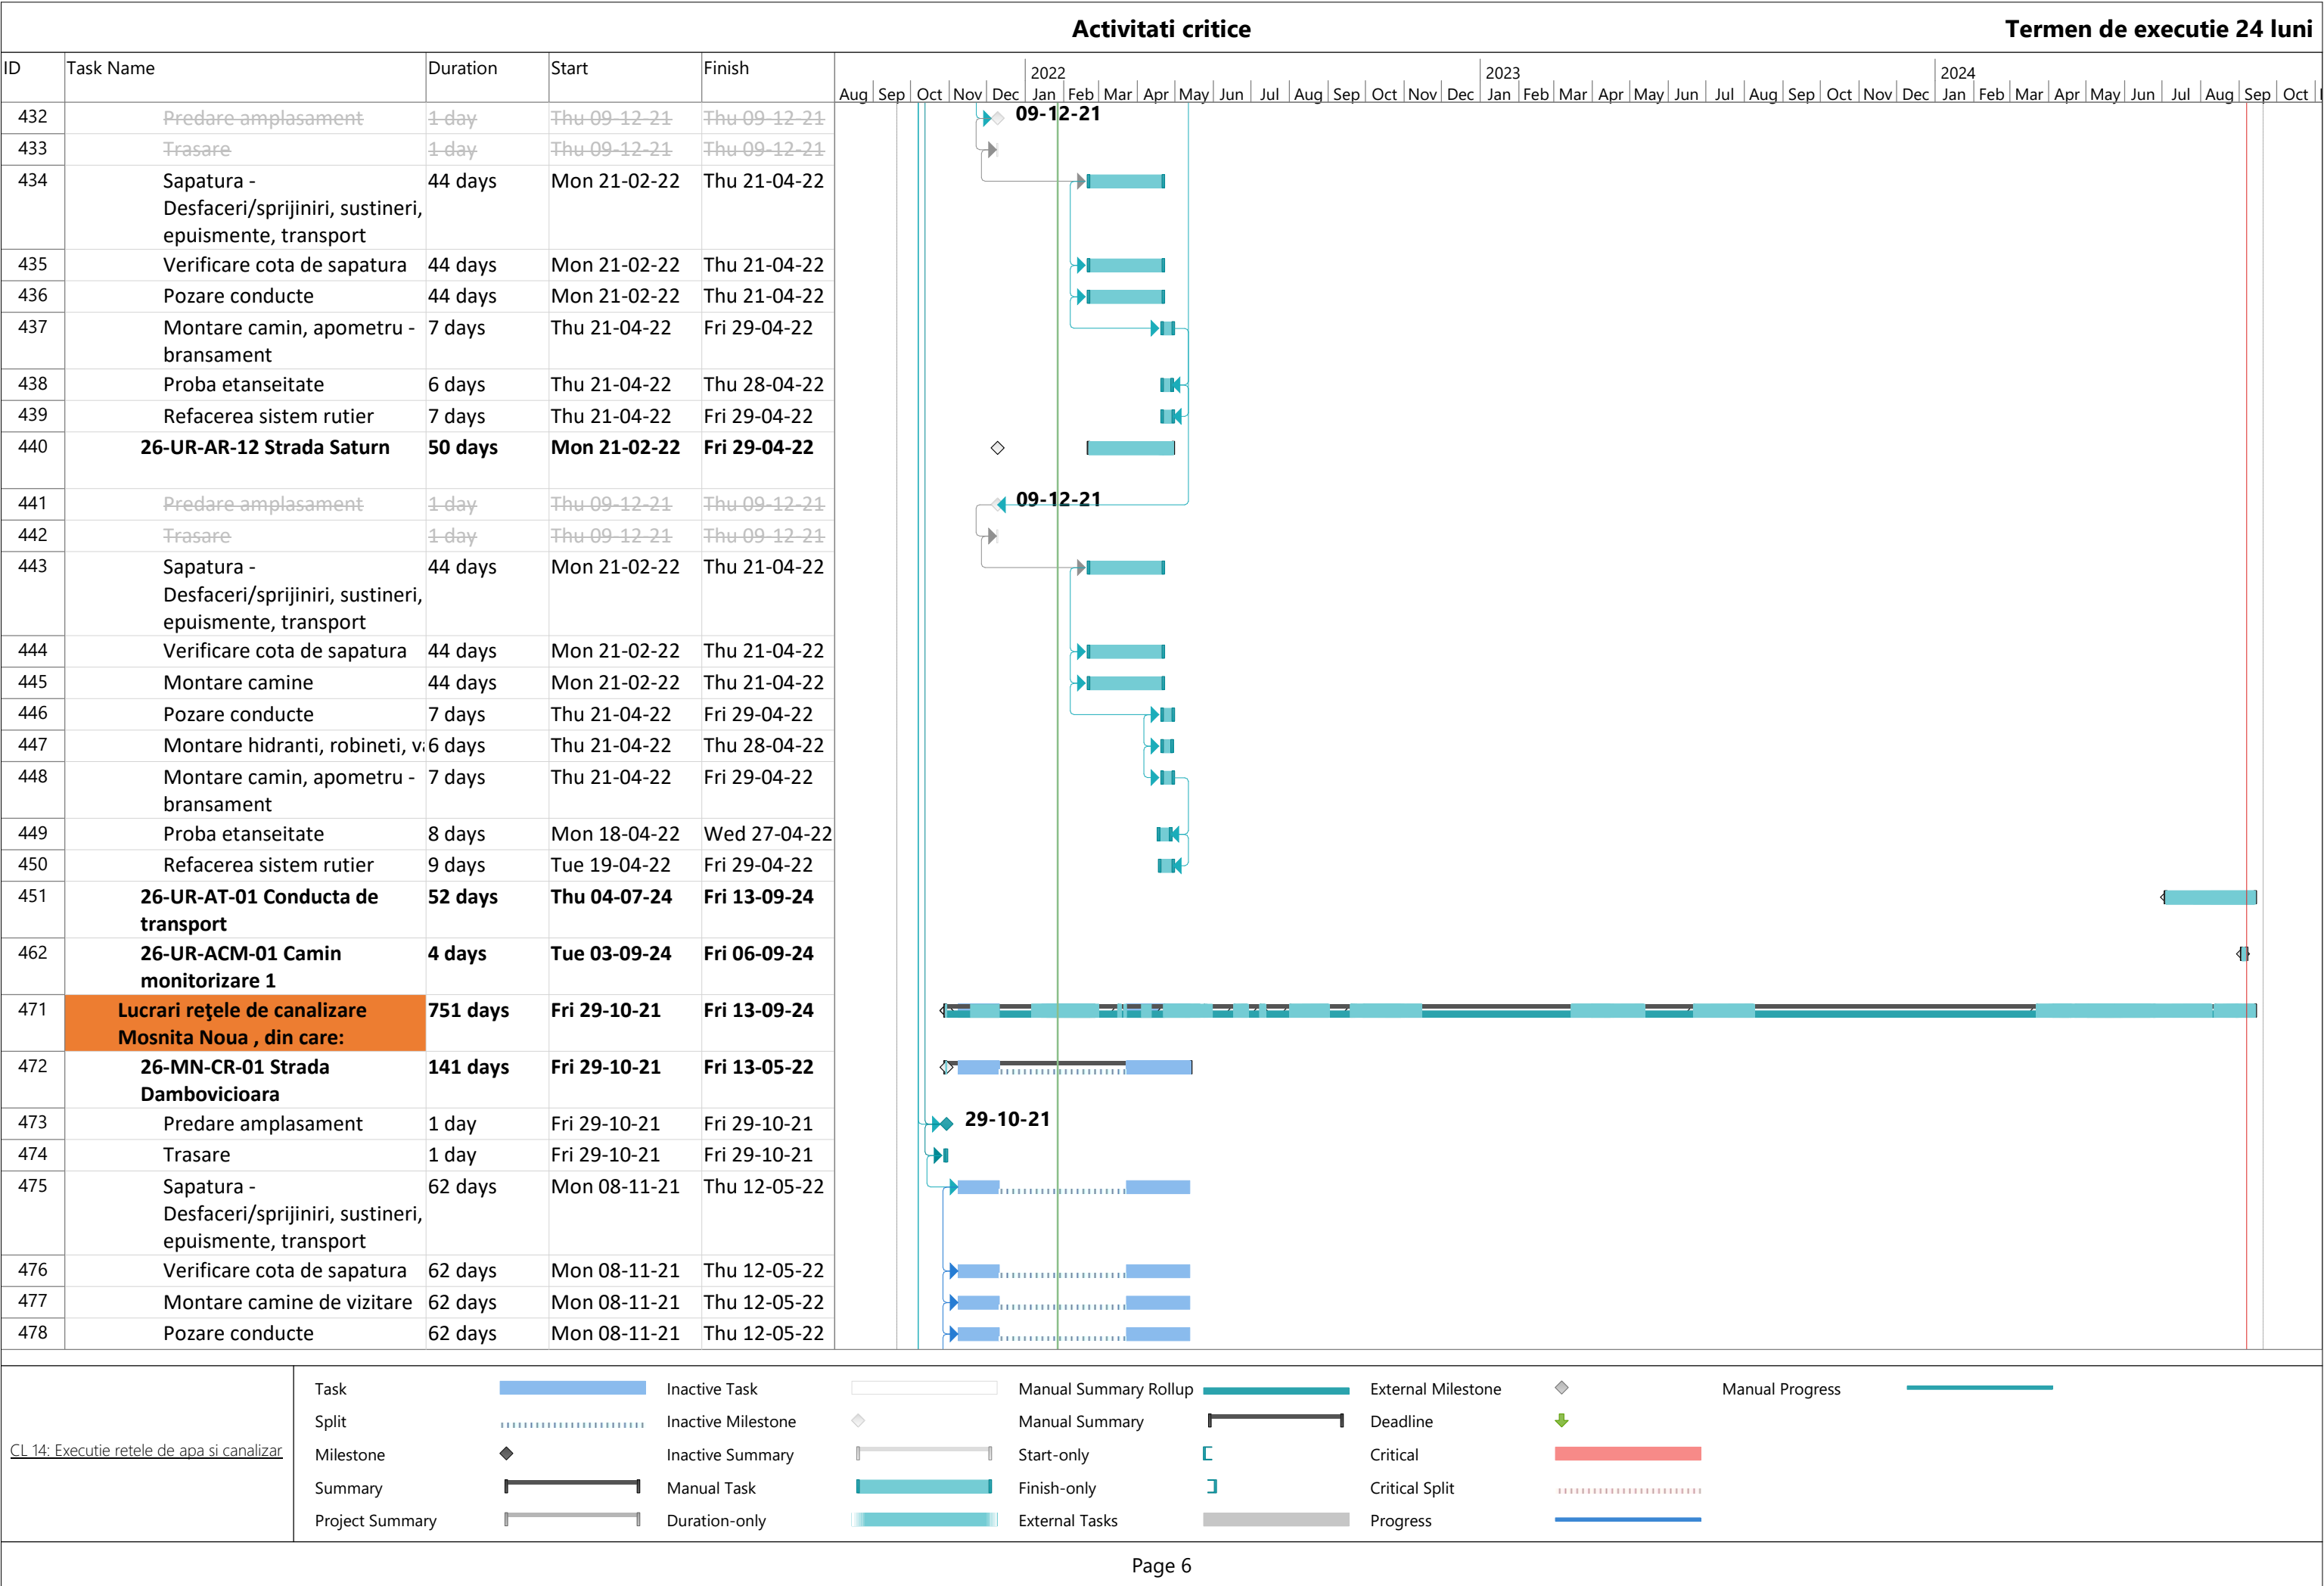

Activitati critice						Termen de executie 24 luni																																						
ID	Task Name	Duration	Start	Finish																																								
					2022												2023												2024															
					Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	
479	Montare racorduri canalizare (piesa + camin de	62 days	Mon 08-11-21	Thu 12-05-22																																								
480	Proba etanseitate	38 days	Wed 23-03-22	Fri 13-05-22																																								
481	Refacerea sistem rutier	24 days	Tue 12-04-22	Fri 13-05-22																																								
482	26-MN-CR-02 Strada Ghirlandei	126 days	Fri 29-10-21	Fri 22-04-22																																								
483	Predare amplasament	1 day	Fri 29-10-21	Fri 29-10-21																																								
484	Trasare	1 day	Fri 29-10-21	Fri 29-10-21																																								
485	Sapatura - Desfaceri/sprijiniri, sustineri, epuismnte, transport	47 days	Mon 08-11-21	Thu 21-04-22																																								
486	Verificare cota de sapatura	47 days	Mon 08-11-21	Thu 21-04-22																																								
487	Montare camine de vizitare	47 days	Mon 08-11-21	Thu 21-04-22																																								
488	Pozare conducte	47 days	Mon 08-11-21	Thu 21-04-22																																								
489	Montare racorduri canalizare (piesa + camin de	47 days	Mon 08-11-21	Thu 21-04-22																																								
490	Proba etanseitate	22 days	Thu 24-03-22	Fri 22-04-22																																								
491	Refacerea sistem rutier	16 days	Fri 01-04-22	Fri 22-04-22																																								
492	26-MN-CR-03 Strada 4	19 days	Fri 22-03-24	Wed 17-04-24																																								
503	26-MN-CR-04 Strada Pietroasa	118 days	Fri 29-10-21	Tue 12-04-22																																								
504	Predare amplasament	1 day	Fri 29-10-21	Fri 29-10-21																																								
505	Trasare	1 day	Fri 29-10-21	Fri 29-10-21																																								
506	Sapatura - Desfaceri/sprijiniri, sustineri, epuismnte, transport	23 days	Thu 18-11-21	Mon 11-04-22																																								
507	Verificare cota de sapatura	23 days	Thu 18-11-21	Mon 11-04-22																																								
508	Montare camine de vizitare	23 days	Thu 18-11-21	Mon 11-04-22																																								
509	Pozare conducte	23 days	Thu 18-11-21	Mon 11-04-22																																								
510	Montare racorduri canalizare (piesa + camin de	23 days	Thu 18-11-21	Mon 11-04-22																																								
511	Proba etanseitate	17 days	Mon 29-11-21	Tue 12-04-22																																								
512	Refacerea sistem rutier	7 days	Mon 04-04-22	Tue 12-04-22																																								
513	26-MN-CR-05 Strada Orsova	24 days	Mon 01-08-22	Thu 01-09-22																																								
524	26-MN-CR-06 Strada Georgeta	49 days	Tue 24-05-22	Fri 29-07-22																																								
525	Predare amplasament	1 day	Fri 29-10-21	Fri 29-10-21																																								
526	Trasare	1 day	Fri 29-10-21	Fri 29-10-21																																								
527	Sapatura - Desfaceri/sprijiniri, sustineri, epuismnte, transport	31 days	Fri 14-01-22	Fri 25-02-22																																								
528	Verificare cota de sapatura	31 days	Fri 14-01-22	Fri 25-02-22																																								
529	Montare camine de vizitare	31 days	Fri 14-01-22	Fri 25-02-22																																								
CL 14: Executie retele de apa si canalizar		Task Inactive Task	Milestone Inactive Milestone	Summary Manual Task	Project Summary Duration-only																																							
		Split Inactive Milestone	Milestone Inactive Summary	Summary Manual Task	Project Summary Duration-only																																							
		Milestone Inactive Summary	Summary Manual Task	Project Summary Duration-only																																								
		Summary Manual Task	Project Summary Duration-only																																									
		Project Summary Duration-only																																										

Page 7

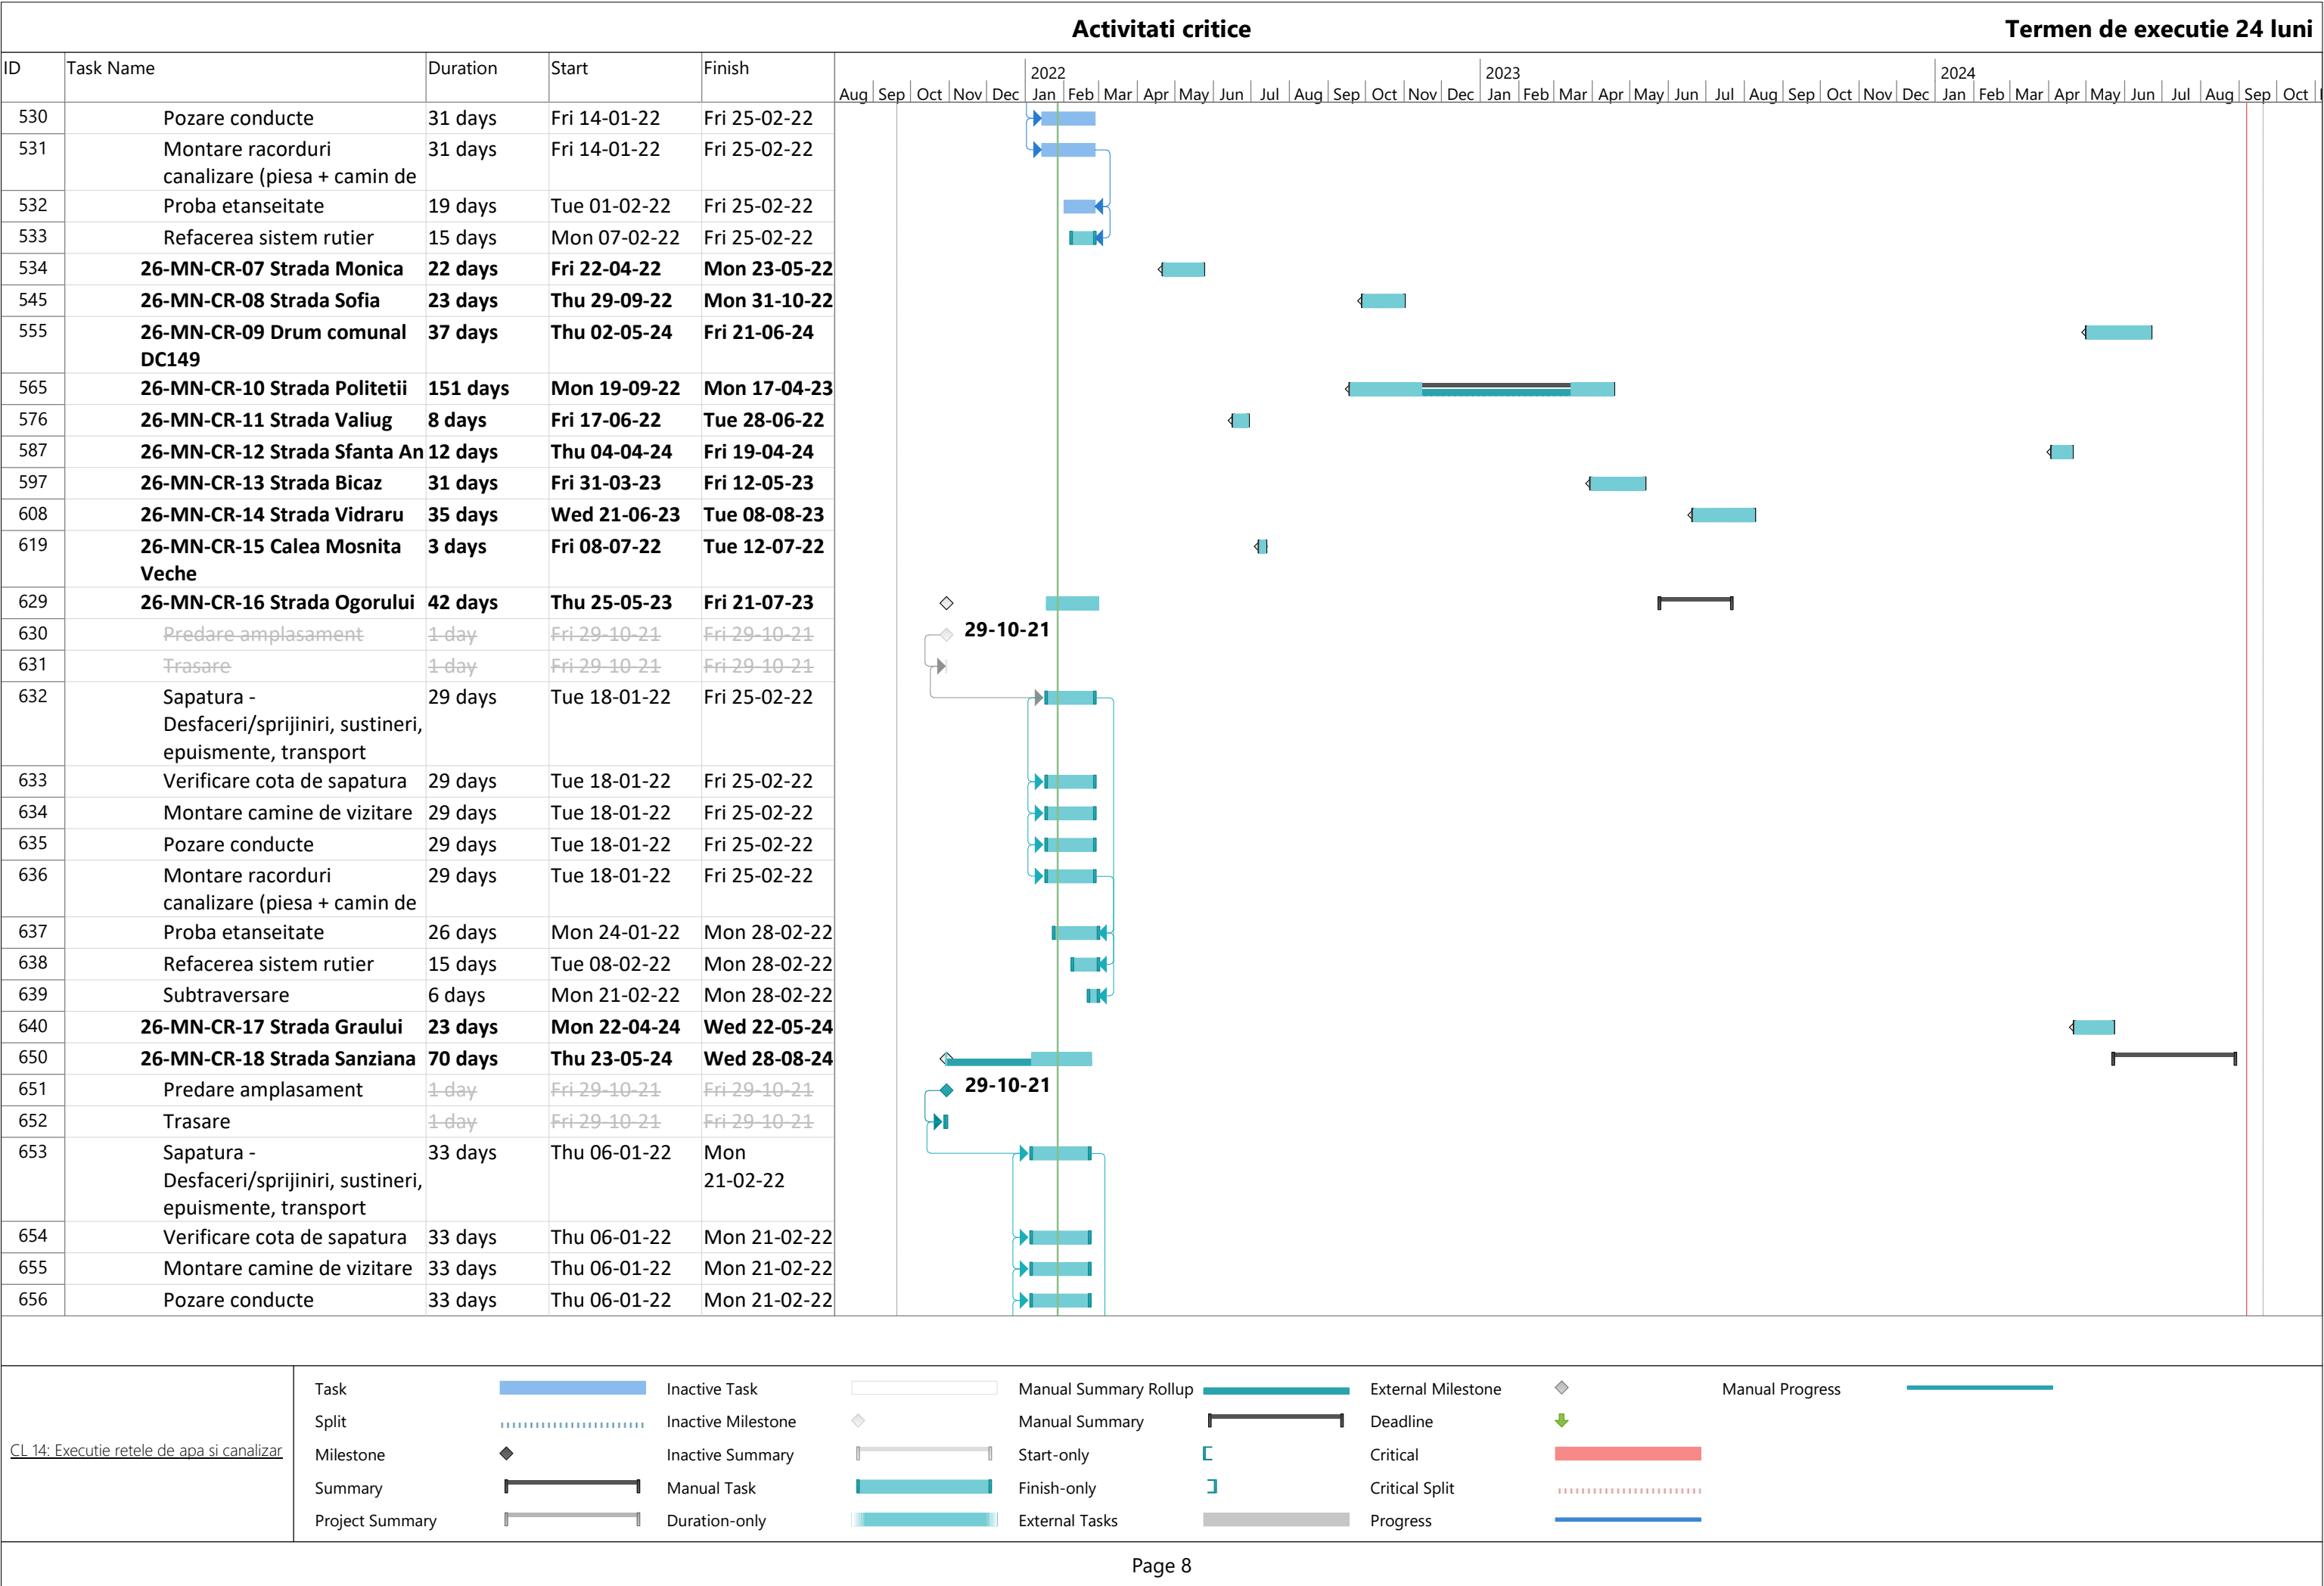



Page 9
